


三洲电排站


清疏大南渠, 清疏总长度2900米

清疏明渠水仙花, 总长450米  
渠道均宽4米


清疏伦垌水库排洪渠, 清疏总长度800米

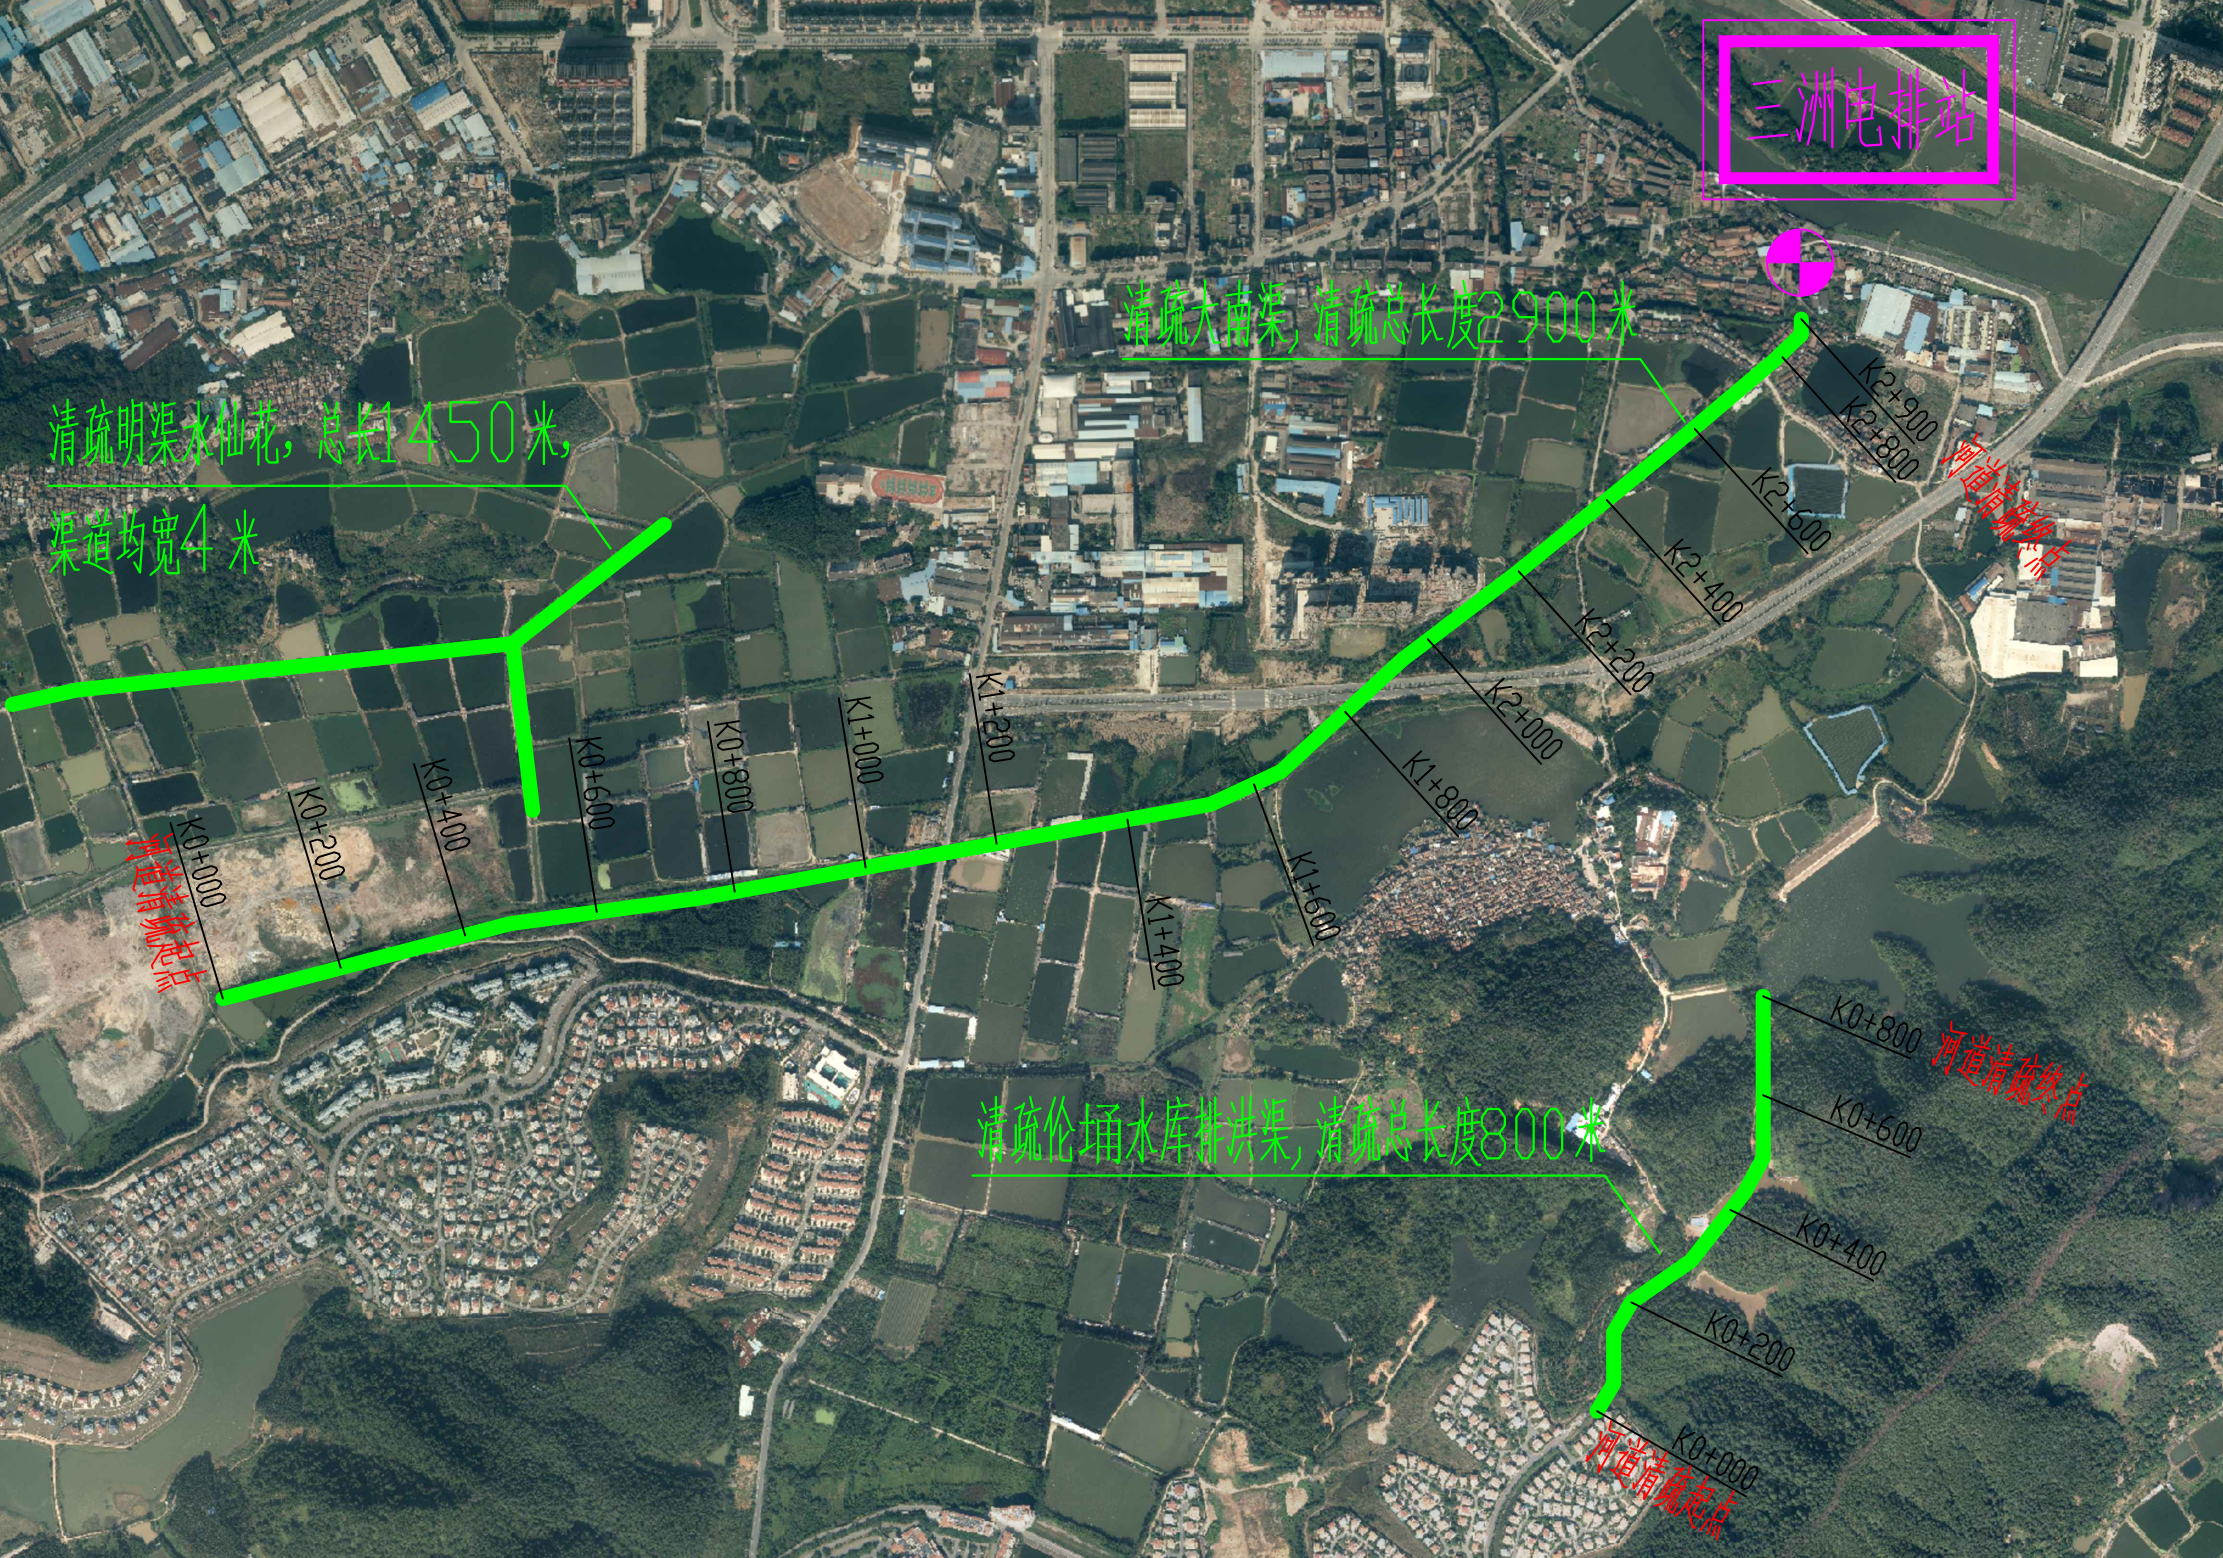


K0+000




K0+200




K0+400




K0+600




K0+800




K1+000



K1+200




K1+400




大南渠清淤横断面图(1/2)


K1+600




K1+800




K2+000




K2+200




K2+400




K2+600




K2+800



K2+900




大南渠清淤横断面图(2/2)

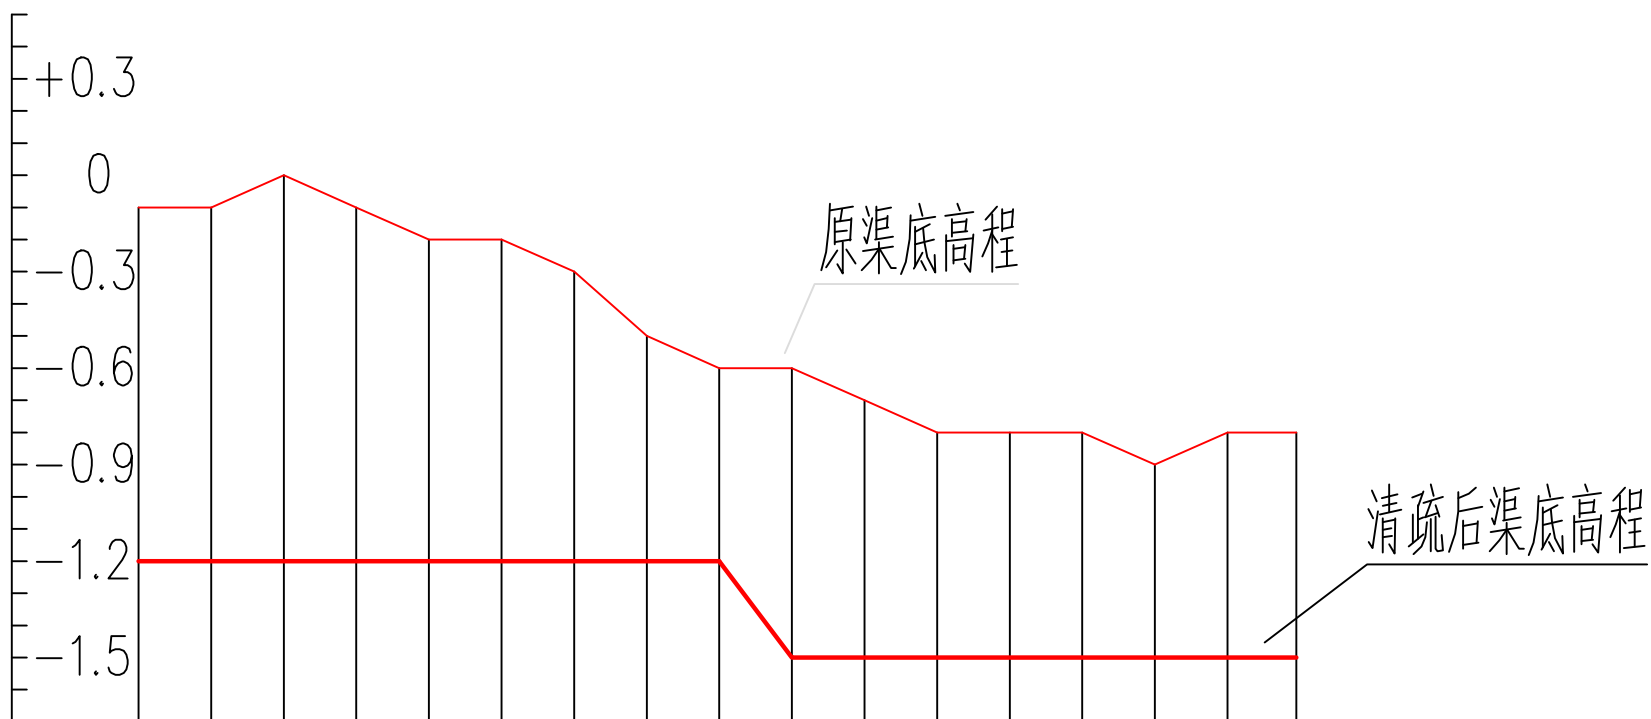


原渠底高程	-0.1	-0.1	0	-0.1	-0.2	-0.2	-0.3	-0.5	-0.6	-0.6	-0.7	-0.8	-0.8	-0.9	-0.8	-0.8
清疏后渠底高程	-1.2	-1.2	-1.2	-1.2	-1.2	-1.2	-1.2	-1.2	-1.2	-1.5	-1.5	-1.5	-1.5	-1.5	-1.5	-1.5
里程	K0+000	K0+200	K0+400	K0+600	K0+800	K1+000	K1+200	K1+400	K1+600	K1+800	K2+000	K2+200	K2+400	K2+600	K2+800	K2+900

大南渠清淤纵断面图(1/1)


K0+000




K0+200




K0+400



K0+600



K0+800



伦埔水库排洪渠清淤断面图(1/1)

### 大南渠清淤工程量计算表

桩号	间距 L(m)	清淤		
		A	$\bar{A}$	$V(m^3)$
K0+000		3.96		
K0+200	200	4.51	4.235	847
K0+400	200	6.24	5.375	1075
K0+600	200	7.81	7.025	1405
K0+800	200	9	8.405	1681
K1+000	200	10	9.5	1900
K1+200	200	9.81	9.905	1981
K1+400	200	7.49	8.65	1730
K1+600	200	6.96	7.225	1445
K1+800	200	11.61	9.285	1857
K2+000	200	11.04	11.325	2265
K2+200	200	10.99	11.015	2203
K2+400	200	12.39	11.69	2338
K2+600	200	10.56	11.475	2295
K2+800	200	11.69	11.125	2225
K2+900	100	10.99	11.34	1134
工程量				25381

### 伦涌水库排洪渠清淤工程量计算表

桩号	间距 L(m)	清淤		
		A	$\bar{A}$	$V(m^3)$
K0+000		4		
K0+200	200	4	4	800
K0+400	200	5	4.5	900
K0+600	200	5	5	1000
K0+800	200	5	5	1000
工程量				3700

清淤工程量计算表
